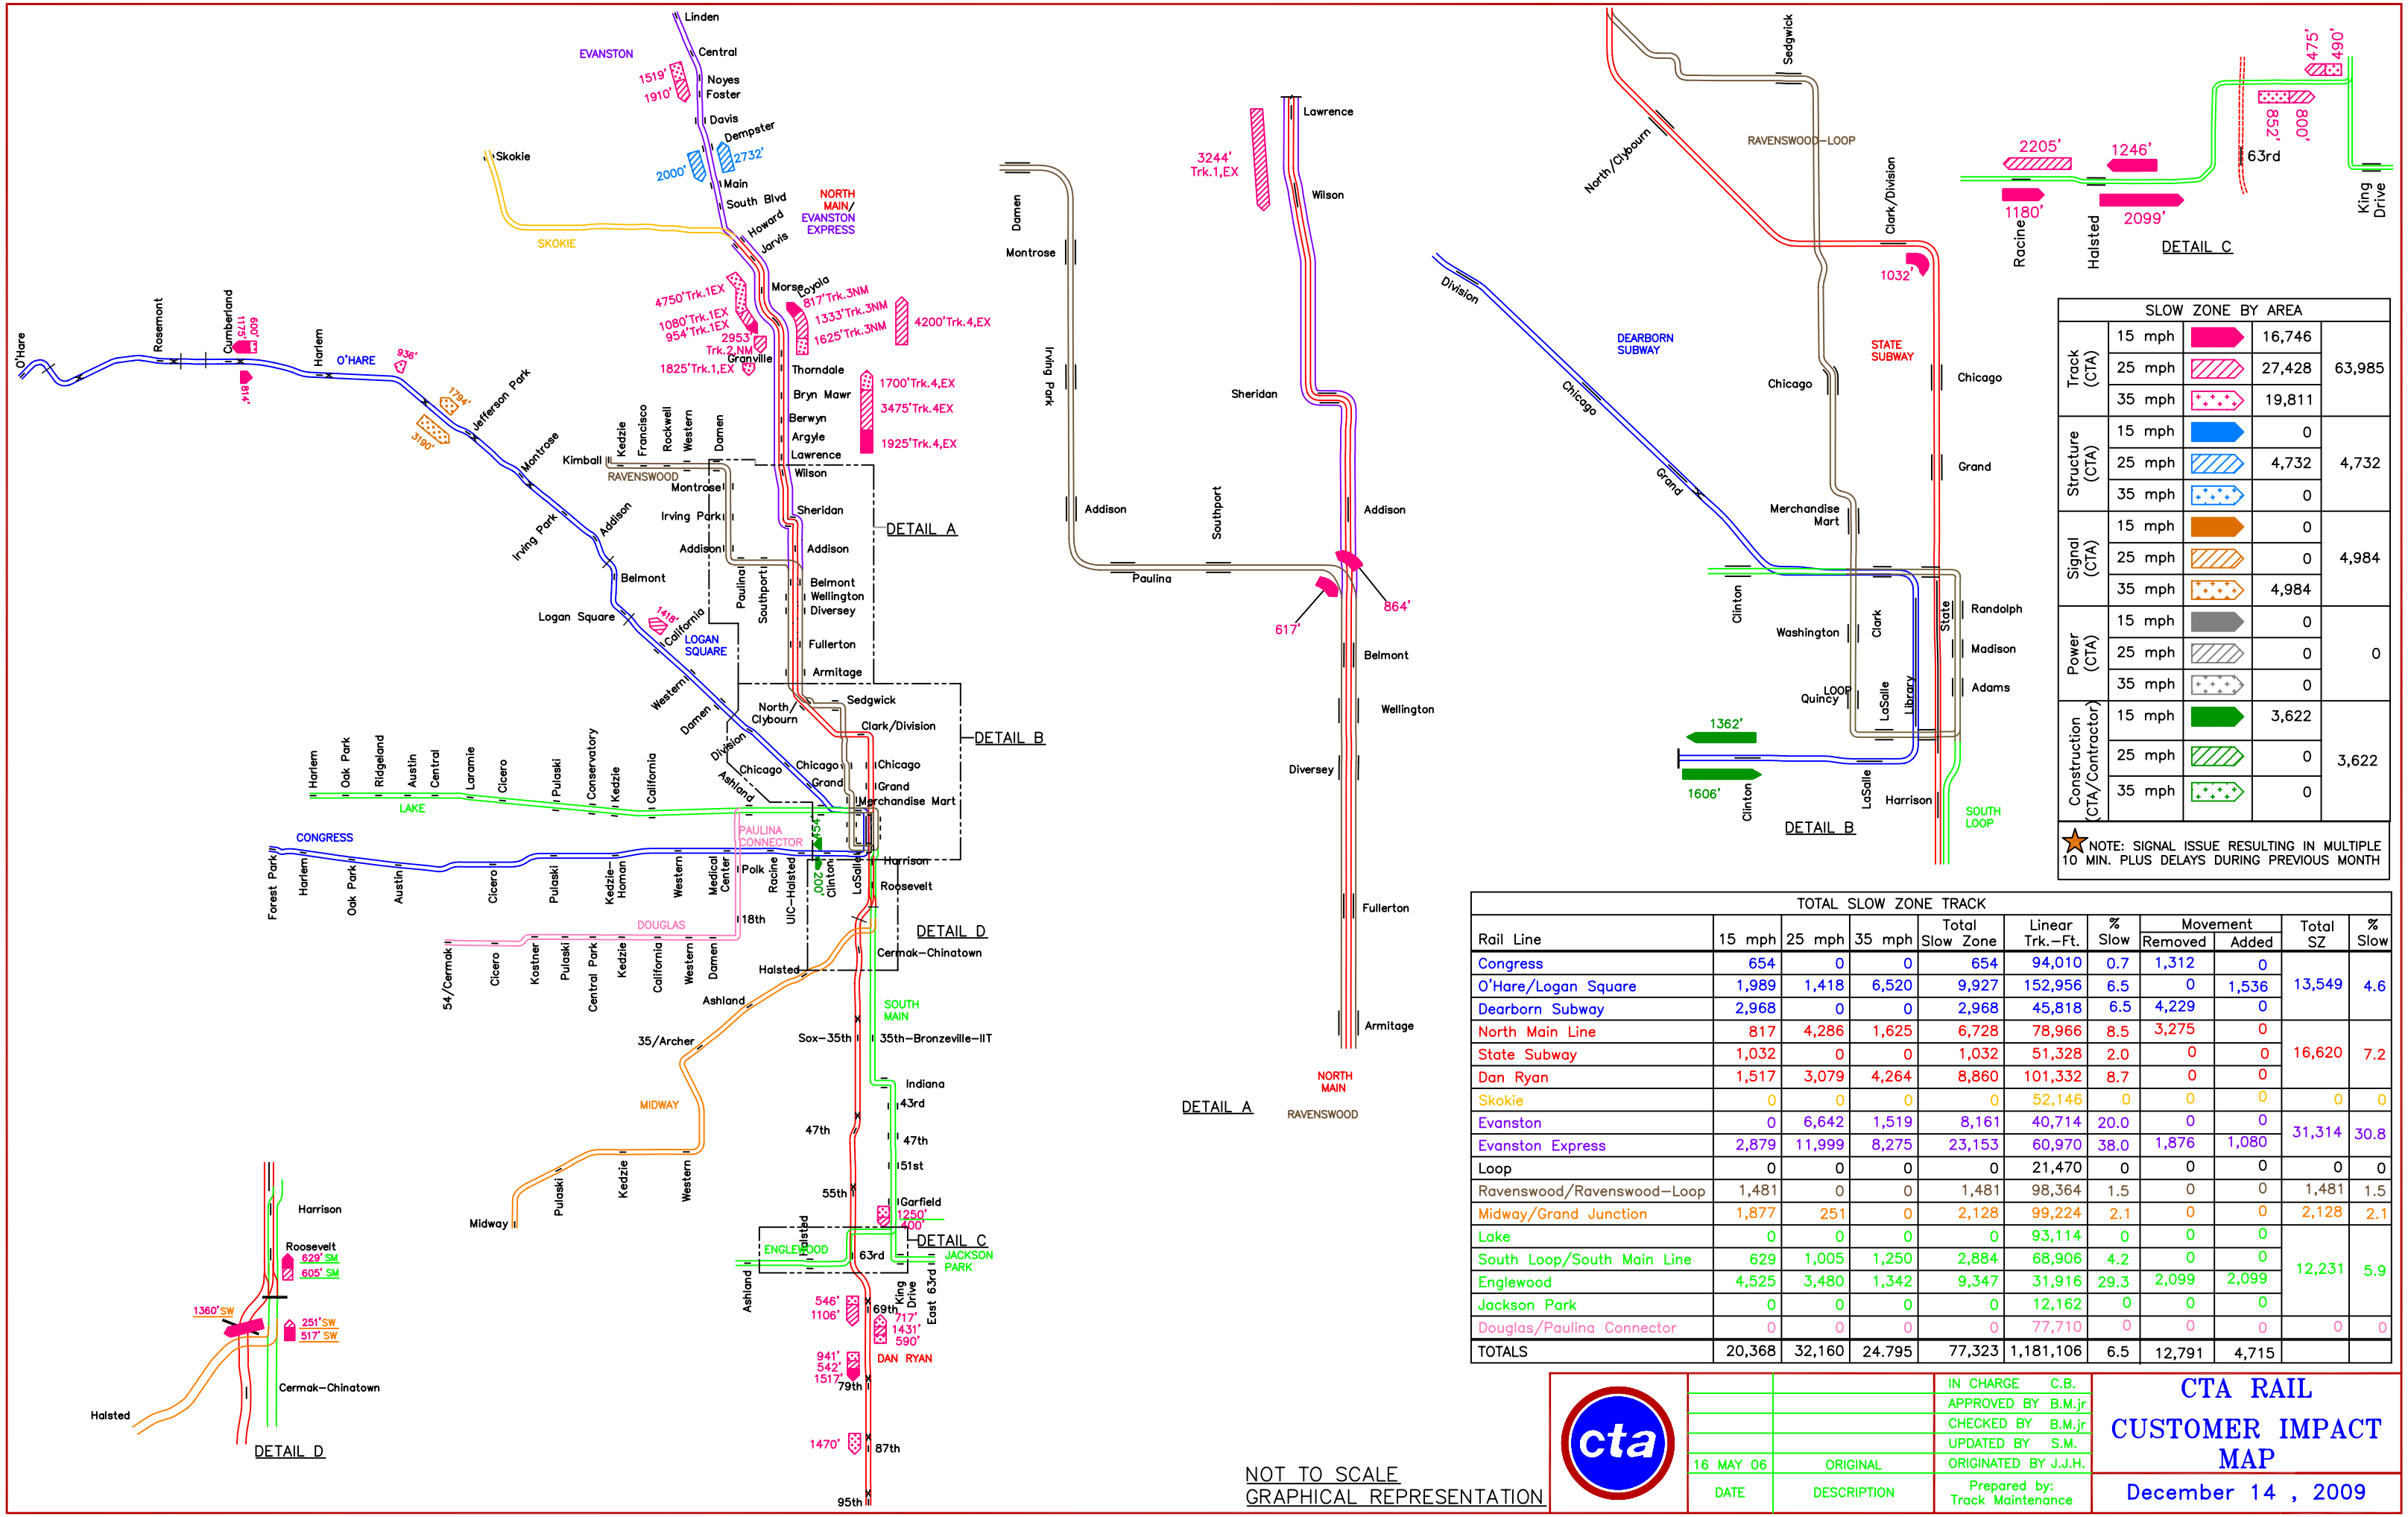

SLOW ZONE BY AREA				
Track (CTA)	15 mph		16,746	63,985
	25 mph		27,428	
	35 mph		19,811	
Structure (CTA)	15 mph		0	4,732
	25 mph		4,732	
	35 mph		0	
Signal (CTA)	15 mph		0	4,984
	25 mph		0	
	35 mph		4,984	
Power (CTA)	15 mph		0	0
	25 mph		0	
	35 mph		0	
Construction (CTA/Contractor)	15 mph		3,622	3,622
	25 mph		0	
	35 mph		0	

★ NOTE: SIGNAL ISSUE RESULTING IN MULTIPLE 10 MIN. PLUS DELAYS DURING PREVIOUS MONTH

TOTAL SLOW ZONE TRACK

Rail Line	15 mph	25 mph	35 mph	Total Slow Zone	Linear Trk.–Ft.	% Slow	Movement Removed	Movement Added	Total SZ	% Slow
Congress	654	0	0	654	94,010	0.7	1,312	0	13,549	4.6
O'Hare/Logan Square	1,989	1,418	6,520	9,927	152,956	6.5	0	1,536		
Dearborn Subway	2,968	0	0	2,968	45,818	6.5	4,229	0		
North Main Line	817	4,286	1,625	6,728	78,966	8.5	3,275	0	16,620	7.2
State Subway	1,032	0	0	1,032	51,328	2.0	0	0		
Dan Ryan	1,517	3,079	4,264	8,860	101,332	8.7	0	0		
Skokie	0	0	0	0	52,146	0	0	0	0	0
Evanston	0	6,642	1,519	8,161	40,714	20.0	0	0	31,314	30.8
Evanston Express	2,879	11,999	8,275	23,153	60,970	38.0	1,876	1,080		
Loop	0	0	0	0	21,470	0	0	0	0	0
Ravenswood/Ravenswood–Loop	1,481	0	0	1,481	98,364	1.5	0	0	1,481	1.5
Midway/Grand Junction	1,877	251	0	2,128	99,224	2.1	0	0	2,128	2.1
Lake	0	0	0	0	93,114	0	0	0	12,231	5.9
South Loop/South Main Line	629	1,005	1,250	2,884	68,906	4.2	0	0		
Englewood	4,525	3,480	1,342	9,347	31,916	29.3	2,099	2,099		
Jackson Park	0	0	0	0	12,162	0	0	0		
Douglas/Paulina Connector	0	0	0	0	77,710	0	0	0	0	0
TOTALS	20,368	32,160	24.795	77,323	1,181,106	6.5	12,791	4,715		

NOT TO SCALE
GRAPHICAL REPRESENTATION

		IN CHARGE C.B.	CTA RAIL CUSTOMER IMPACT MAP
		APPROVED BY B.M.jr	
		CHECKED BY B.M.jr	
		UPDATED BY S.M.	
16 MAY 06	ORIGINAL	ORIGINATED BY J.J.H.	
DATE	DESCRIPTION	Prepared by: Track Maintenance	December 14 , 2009
